**2009 NSV Pilot Study Schedule**
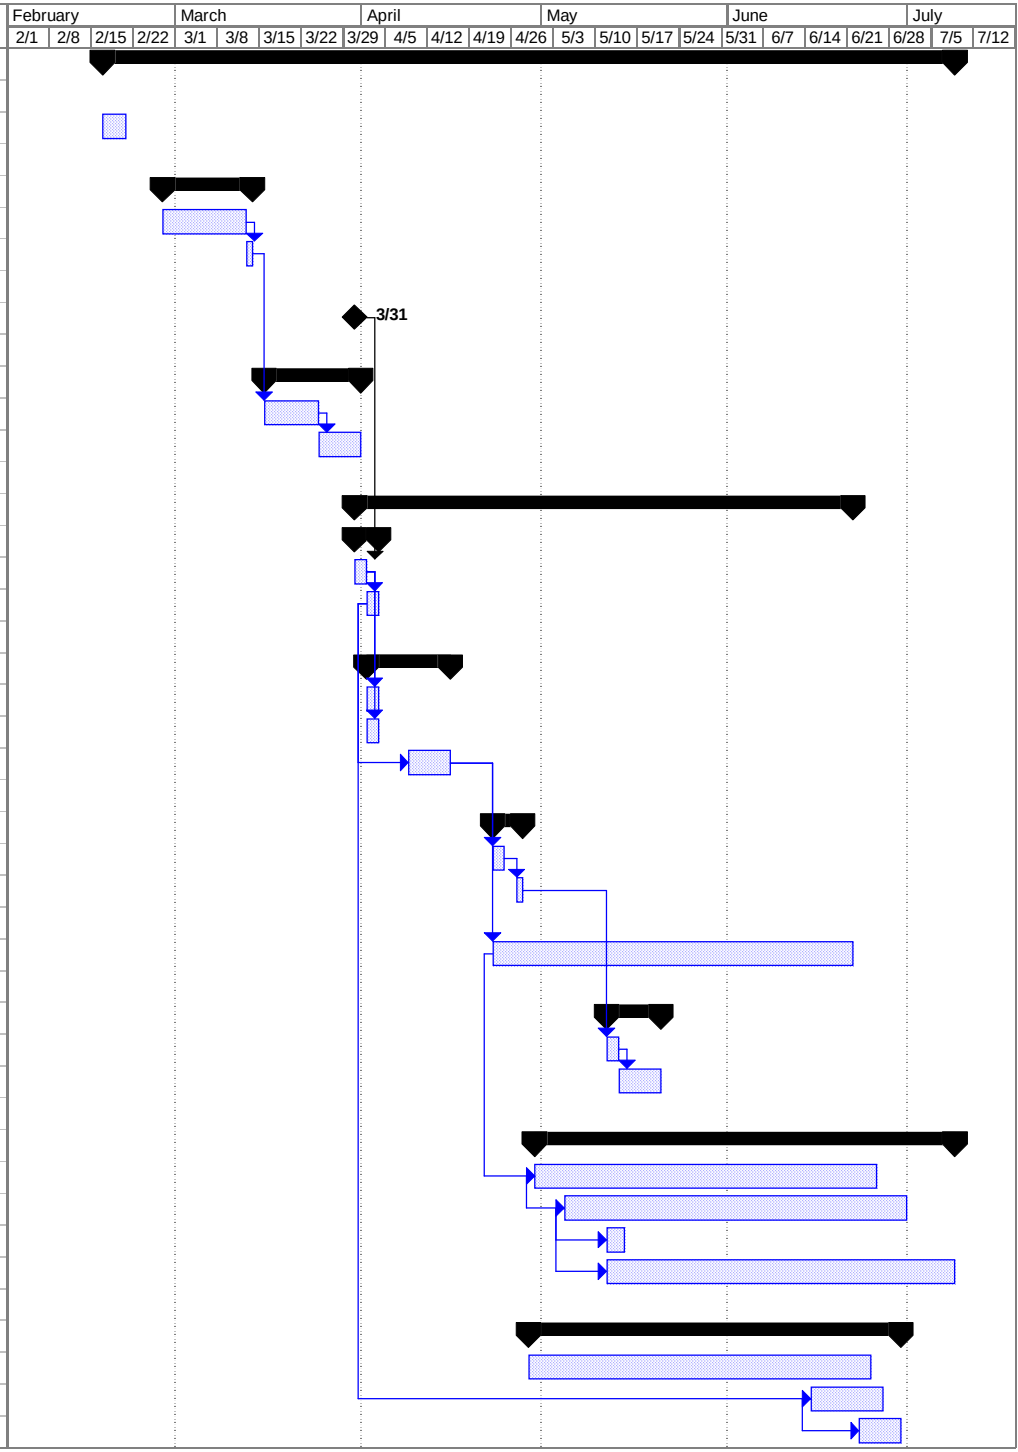
| ID | | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|---|
| 1 | | **NSV Pilot Study - Data Collection** | **100 days** | **Tue 2/17/09** | **Wed 7/8/09** | |
| 2 | | | | | | |
| 3 | | Print Envelopes (9x12, #10, BRE) | 4 days | Tue 2/17/09 | Fri 2/20/09 | |
| 4 | | | | | | |
| 5 | | **Final Communication Letters** | **11 days** | **Fri 2/27/09** | **Fri 3/13/09** | |
| 6 | | VA Reviews and Approves Letters | 10 days | Fri 2/27/09 | Thu 3/12/09 | |
| 7 | | Westat receives final letters | 1 day | Fri 3/13/09 | Fri 3/13/09 | 6 |
| 8 | | | | | | |
| 9 | | Receive OMB Clearance | 0 days | Tue 3/31/09 | Tue 3/31/09 | |
| 10 | | | | | | |
| 11 | | **Produce Print Proofs** | **12 days** | **Mon 3/16/09** | **Tue 3/31/09** | |
| 12 | | Produce Print Proofs | 7 days | Mon 3/16/09 | Tue 3/24/09 | 7 |
| 13 | | Obtain VA Approval for Proofs | 5 days | Wed 3/25/09 | Tue 3/31/09 | 12 |
| 14 | | | | | | |
| 15 | | **Screener Survey** | **58 days** | **Tue 3/31/09** | **Sun 6/21/09** | |
| 16 | | **Pre-notification** | **4 days** | **Tue 3/31/09** | **Fri 4/3/09** | |
| 17 | | Print pre-notification letters | 2 days | Tue 3/31/09 | Wed 4/1/09 | 9 |
| 18 | | Assemble & mail pre-note letters | 2 days | Thu 4/2/09 | Fri 4/3/09 | 17 |
| 19 | | | | | | |
| 20 | | **Wave 1** | **10 days** | **Thu 4/2/09** | **Wed 4/15/09** | |
| 21 | | **Print Wave 1 surveys & letters** | 2 days | Thu 4/2/09 | Fri 4/3/09 | 17 |
| 22 | | Print inserts | 2 days | Thu 4/2/09 | Fri 4/3/09 | 17 |
| 23 | | **Assemble & mail Wave 1 packets** | 5 days | Thu 4/9/09 | Wed 4/15/09 | 18SS+1 wk |
| 24 | | | | | | |
| 25 | | **Reminder Postcards** | **3 days** | **Thu 4/23/09** | **Mon 4/27/09** | |
| 26 | | Print Postcards | 2 days | Thu 4/23/09 | Fri 4/24/09 | 23FS+1 wk |
| 27 | | Mail Postcards | 1 day | Mon 4/27/09 | Mon 4/27/09 | 26 |
| 28 | | | | | | |
| 29 | | Receive & Process Screener Completes | 60 edays | Wed 4/22/09 | Sun 6/21/09 | 23FS+1 wk |
| 30 | | | | | | |
| 31 | | **Wave 2** | **7 days** | **Tue 5/12/09** | **Wed 5/20/09** | |
| 32 | | Print Wave 2 surveys & letters | 2 days | Tue 5/12/09 | Wed 5/13/09 | 27FS+2 wks |
| 33 | | **Assemble & mail Wave 2 packets** | 5 days | Thu 5/14/09 | Wed 5/20/09 | 32 |
| 34 | | | | | | |
| 35 | | **Extended Survey** | **48 days** | **Thu 4/30/09** | **Wed 7/8/09** | |
| 36 | | Print Wave 1 surveys & letters | 2 mons | Thu 4/30/09 | Thu 6/25/09 | 29SS+1 wk |
| 37 | | Assemble & mail Wave 1 packets | 2 mons | Tue 5/5/09 | Tue 6/30/09 | 36SS+3 days |
| 38 | | Print & Mail Postcards | 3 days | Tue 5/12/09 | Thu 5/14/09 | 37SS+1 wk |
| 39 | | Receive & Process Extended Completes | 40 days | Tue 5/12/09 | Wed 7/8/09 | 37SS+1 wk |
| 40 | | | | | | |
| 41 | | **De-Briefings & Data Analysis** | **43 days** | **Wed 4/29/09** | **Mon 6/29/09** | |
| 42 | | Conduct DeBriefing Interviews | 2 mons | Wed 4/29/09 | Wed 6/24/09 | |
| 43 | | Analyze Pilot Data | 10 days | Mon 6/15/09 | Fri 6/26/09 | 18SS+74 edays |
| 44 | | Develop OMB Briefing for the Main Survey | 5 days | Tue 6/23/09 | Mon 6/29/09 | 43SS+6 days |
